


**RELIEF WELL #2**  
Development Driller II

**DISCOVERER ENTERPRISE DRILL SHIP**  
Original MC 252 #1 Subsea Containment

**RELIEF WELL #1**  
Development Driller III  
Spudded May 2nd at 15:27hrs

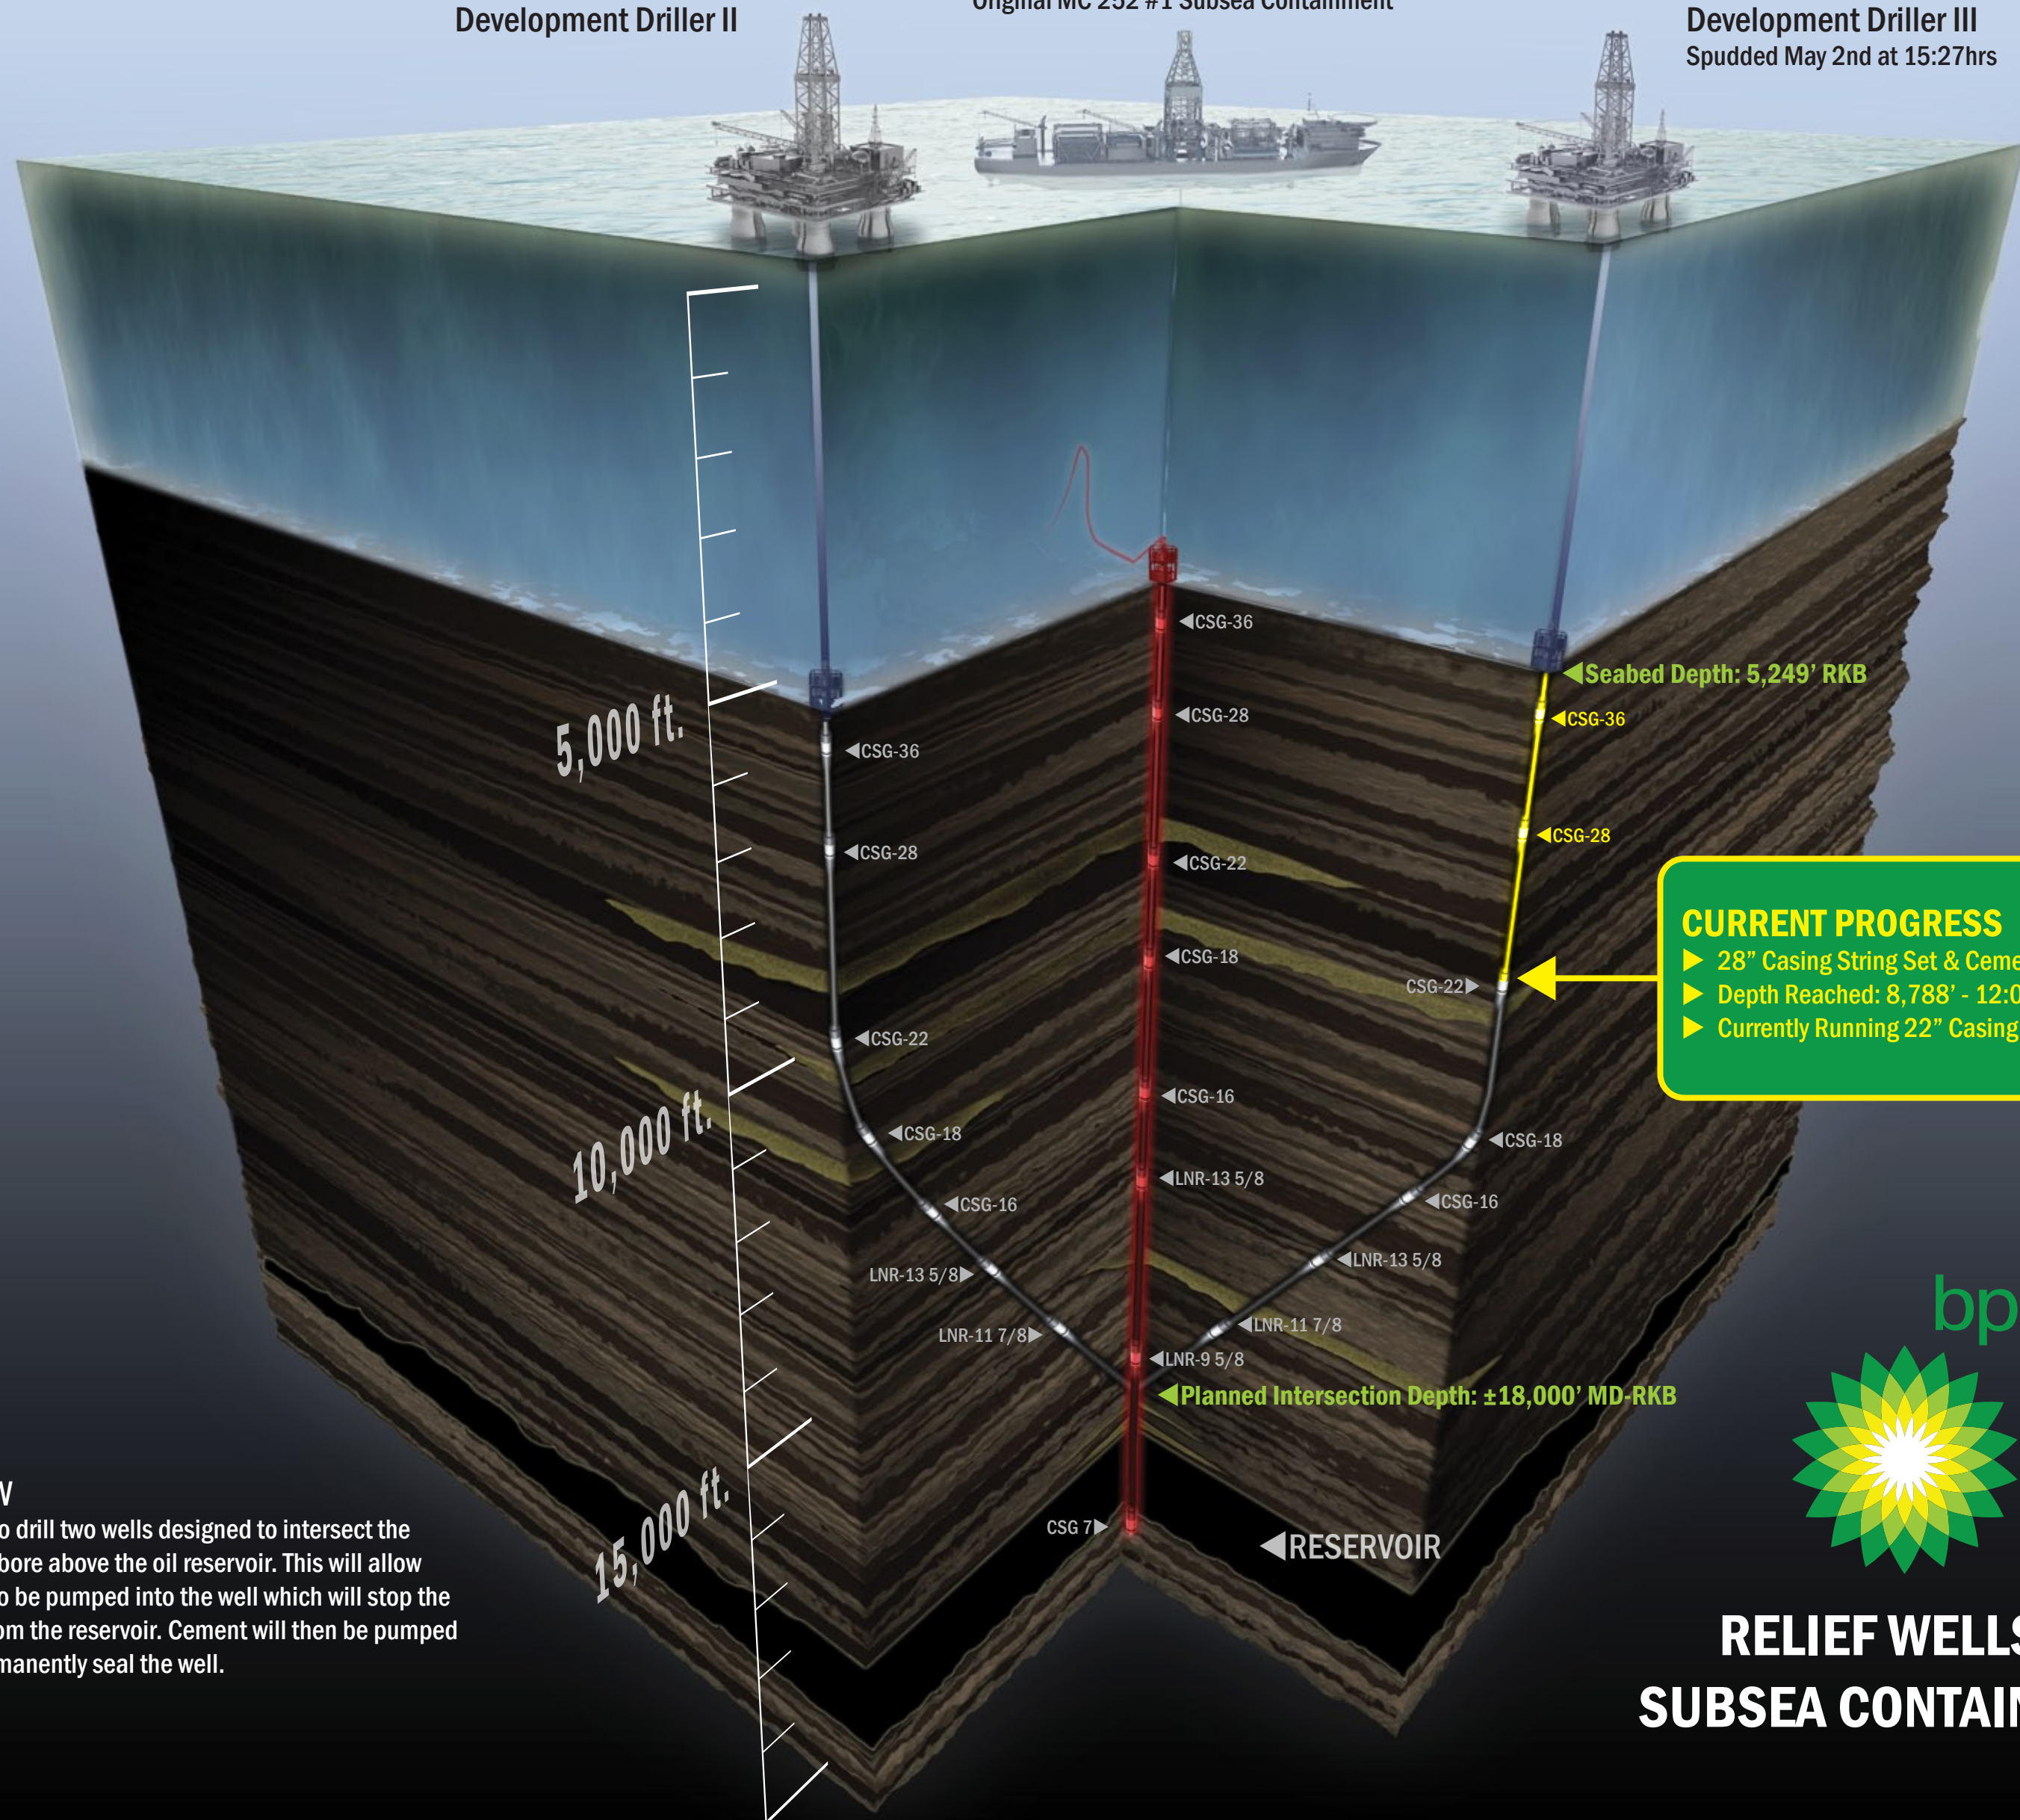


**CURRENT PROGRESS**

- ▶ 28" Casing String Set & Cemented In Place
- ▶ Depth Reached: 8,788' - 12:00 May 7th
- ▶ Currently Running 22" Casing - 12:00 May 7th

**OVERVIEW**

BP intends to drill two wells designed to intersect the original wellbore above the oil reservoir. This will allow heavy fluid to be pumped into the well which will stop the flow of oil from the reservoir. Cement will then be pumped down to permanently seal the well.



**RELIEF WELLS &  
SUBSEA CONTAINMENT**
